Delivery 1 - Load 1 of 1 - Artic 13.6 m

5 pallets in 2 of 5 floor positions | 80 forms | tallest column 2455 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

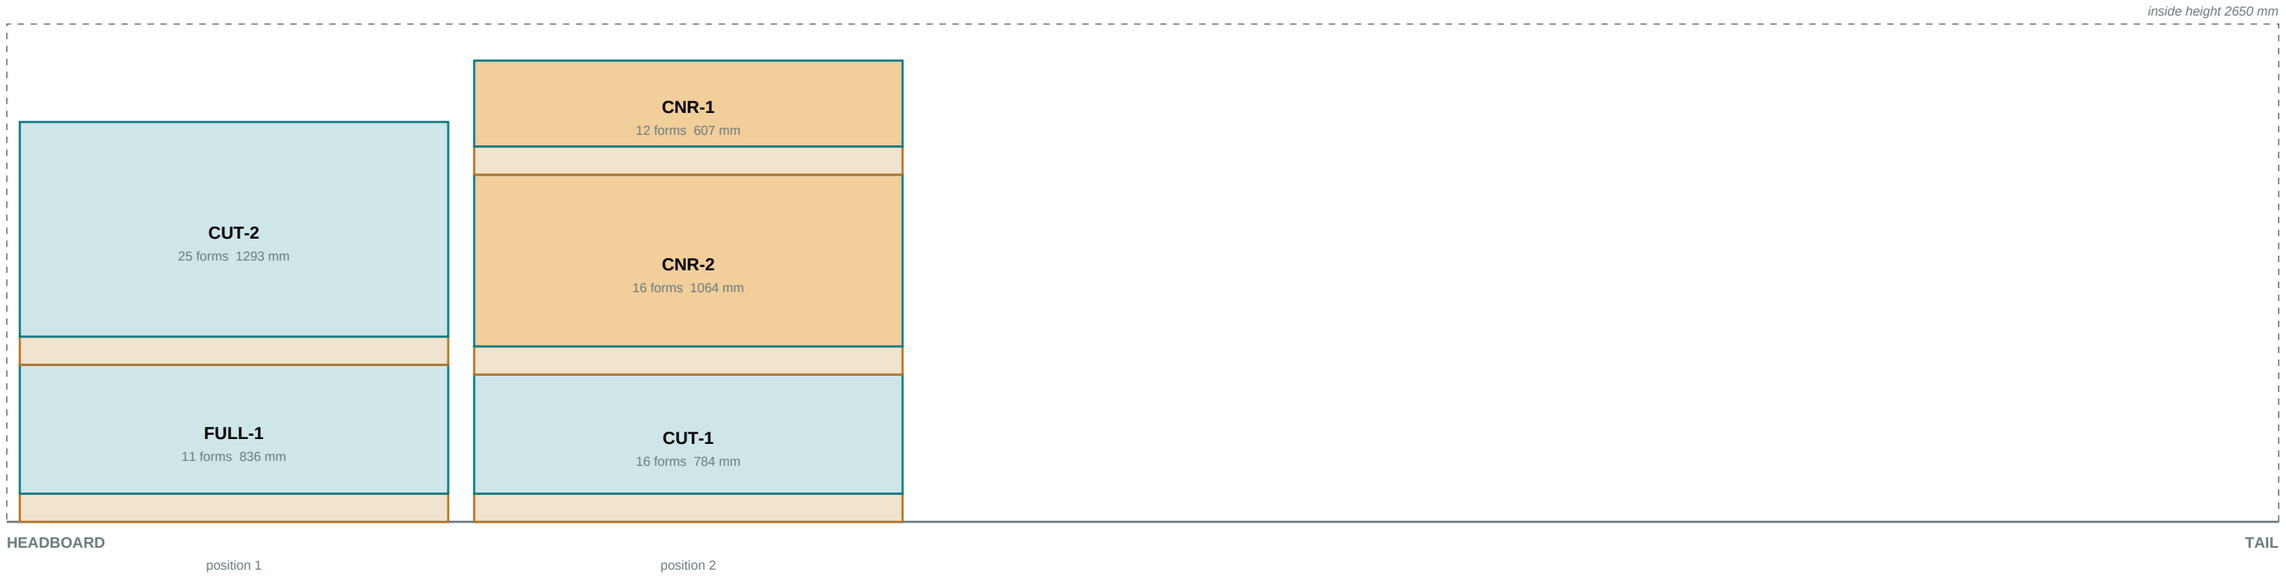

Unload order - 4 of 4 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 6in Std corners 12 forms courses FB courses 1-2
2. CNR-2 6in XR35 corners 16 forms courses FB courses 1-2
3. CUT-1 6in Std straights 16 forms courses FB courses 1-2
4. CUT-2 6in XR35 straights 25 forms courses FB courses 1-2
5. FULL-1 6in XR35 straights 11 forms courses FB course 2

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-081 Lon Eilian, Caernarfon - Plots A-D	FORMS	80
VEHICLE	Artic 13.6 m	POSITIONS	2 of 5
PALLETS	5	TALLEST	2455 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

9 pallets in 5 of 5 floor positions | 226 forms | tallest column 2552 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

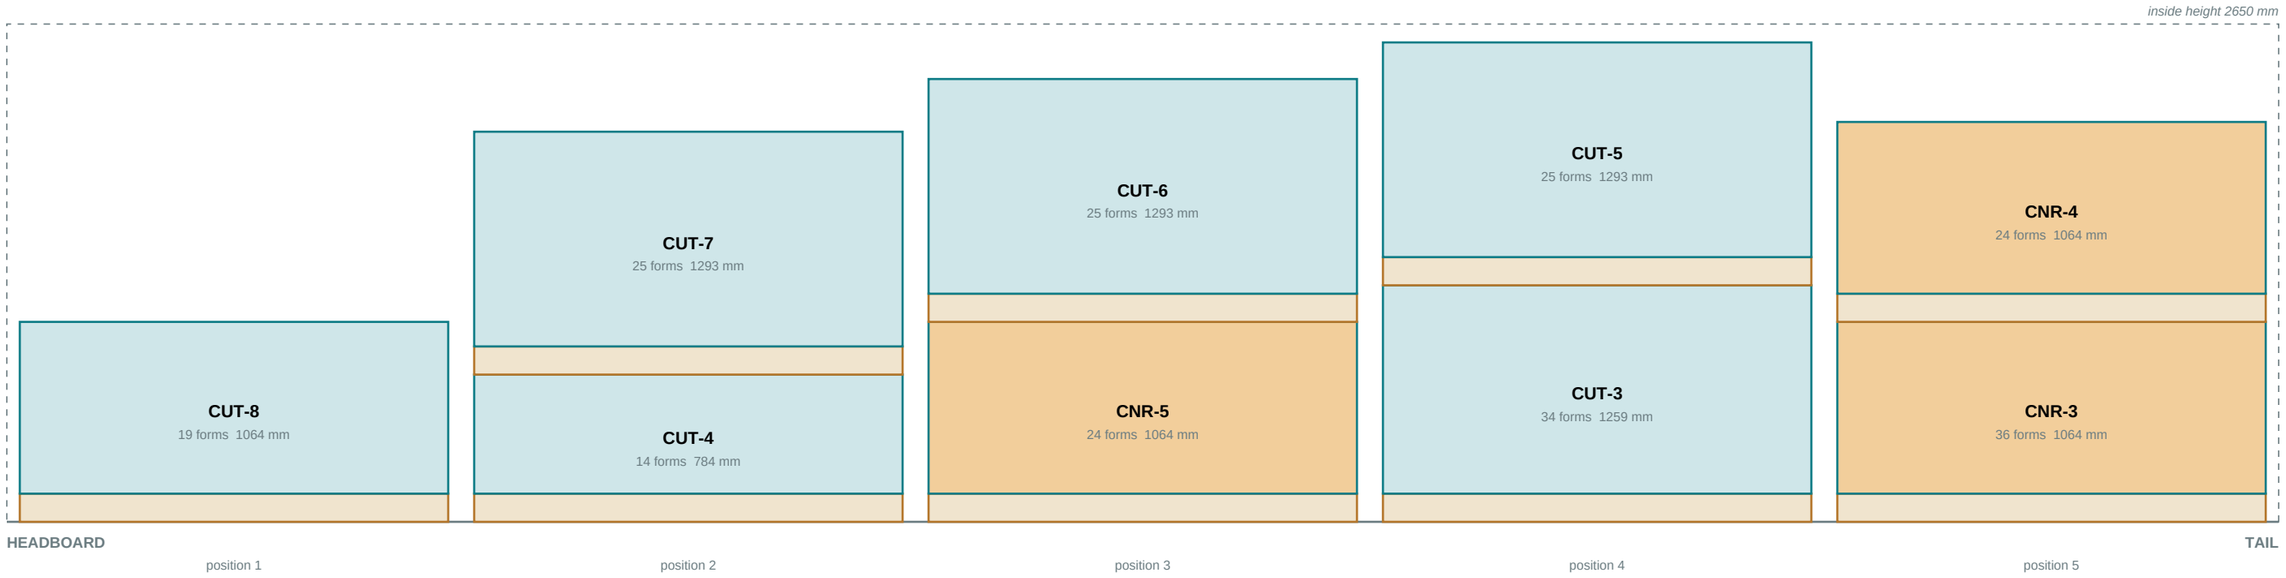

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-4 6in XR35 corners 24 forms courses L1 courses 1-3
2. CNR-3 6in Std corners 36 forms courses L1 courses 1-6
3. CUT-5 6in XR35 straights 25 forms courses L1 courses 1-6
4. CUT-3 6in Std straights 34 forms courses L1 courses 1, 2, 3, 4, 5, 6, 8
5. CUT-6 6in XR35 straights 25 forms courses L1 courses 2-6
6. CNR-5 6in XR35 corners 24 forms courses L1 courses 4-6
7. CUT-7 6in XR35 straights 25 forms courses L1 courses 4-6
8. CUT-4 6in Std straights 14 forms courses L1 courses 5-7
9. CUT-8 6in XR35 straights 19 forms courses L1 course 7

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-081 Lon Eilian, Caernarfon - Plots A-D	FORMS	226
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	9	TALLEST	2552 mm

Delivery 3 - Load 1 of 1 - Artic 13.6 m

9 pallets in 5 of 5 floor positions | 195 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

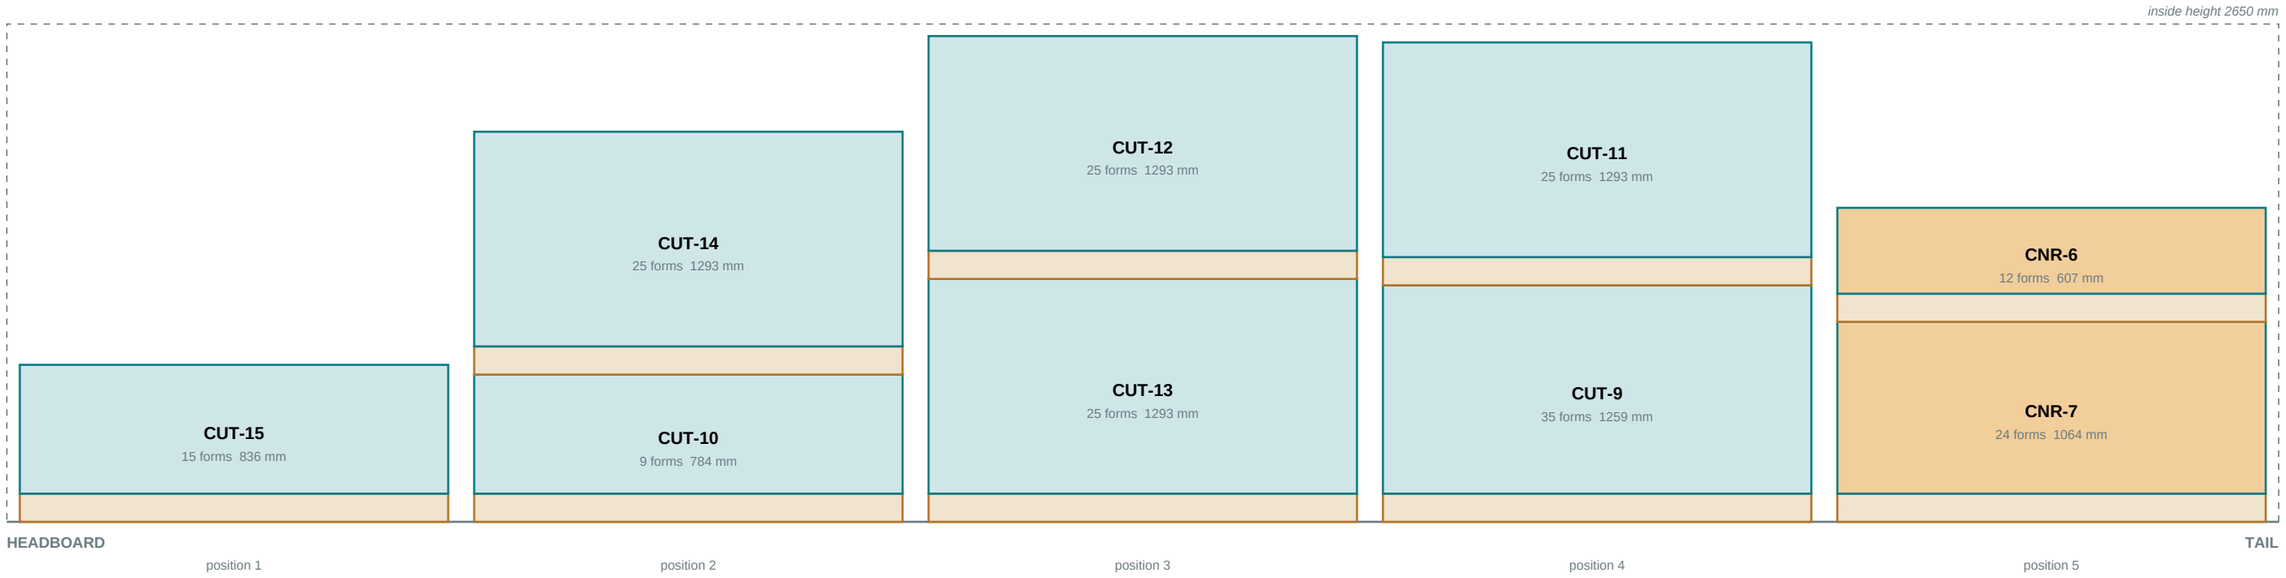

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-6 6in Std corners 12 forms courses L2 courses 1-6
2. CNR-7 6in XR35 corners 24 forms courses L2 courses 1-6
3. CUT-11 6in XR35 straights 25 forms courses L2 courses 1-8
4. CUT-9 6in Std straights 35 forms courses L2 courses 1-12
5. CUT-12 6in XR35 straights 25 forms courses L2 courses 2-7
6. CUT-13 6in XR35 straights 25 forms courses L2 courses 4-10
7. CUT-14 6in XR35 straights 25 forms courses L2 courses 5-11
8. CUT-10 6in Std straights 9 forms courses L2 courses 6-9
9. CUT-15 6in XR35 straights 15 forms courses L2 courses 9-10

Nudura™ **WAGON STACKING PLAN** **D3 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-081 Lon Eilian, Caernarfon - Plots A-D	FORMS	195
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	9	TALLEST	2586 mm
